

**** MCGOUGH BID FORM MUST BE COMPLETED AND RETURNED WITH PRICING ****

TO:	Subcontractor/Supplier	Date:	December 19 th , 2024
FROM:	McGough Construction Brady Snell	DUE DATE:	January 9 th 2025
		DUE TIME:	12:00 PM (Central)
RE:	Fargo Public Schools - Multiple Facility Project		

Tax Exempt **NO****EEO Project Specific Requirements** **NO**

McGough Construction, acting as Construction Manager at Risk, is soliciting **FINAL BID** pricing for the **Fargo Public Schools – Multiple Facility Project** located in Fargo, ND 58105.

Project Description:

The project involves several upgrades and improvements across multiple facilities within the Fargo Public Schools district. This multi-facility project will enhance the educational environment and ensure the facilities meet modern standards and best practices.

Project Locations & RFQ Budgets

- Bennett Elementary
- Carl Ben Eielson Middle School
- Centennial Elementary
- Davies High School
- District Office
- Eagles Elementary
- Lincoln Elementary
- Longfellow Elementary
- North High School
- Operations
- South High School
- Trollwood Performing Arts
- Washington Elementary

Bid package #1 includes all selective demo, misc. metals, earthwork, concrete paving, bituminous paving, track surfacing, playgrounds, landscaping, rough carpentry, finish carpentry, masonry, EIFS, caulking, storefronts, metal roofing, painting, flooring, plumbing, mechanical, & electrical.

Schedule:

A project construction schedule dated **December 16th, 2024** will be available for your use and information. With work commencing as early as April 15th, 2025.

Bidders are required to review this schedule for timeline and durations of your scope of work and include all costs associated with these items. Bidders are required to ensure they have the proper workforce to complete their scope of work in the allotted timeframe.

General Bidder Requirements/Clarifications:

By submitting a proposal, you are acknowledging that you have read and agree to all Bidding Requirements included in the Project Documents available through Smart Bid. This includes but is not limited to:

Documents Requiring Bidder Review and Acceptance:

- Invitation to Bid (this document)
- McGough Sample Subcontract and Exhibits
 - Exhibit A Subcontract General Conditions
 - Exhibit B Insurance Requirements
 - Sample Certificate of Insurance
 - Exhibit C Data Protocol
 - Exhibit D State Specific General Conditions
 - Exhibit E Design Build General Conditions
 - Exhibit F ND Construction Risk Protection Provision
 - Exhibit G McGough Quality Program Requirements
- McGough Safety Standards
- Project Schedule Dated 12/16/2024

Project Document Availability:

Drawings, Specifications and all other project documents are available through iSqFt. If you should have any questions on document access, please contact **Brady Snell** at **701.261.5270** or brady.snell@mcgough.com

Bid Process:

McGough Construction will receive bids until:

Thursday, January 9th 2025 – 12:00 PM (Central)

Sealed proposals can be submitted with the Subject “**FPS- MSA – Bid Package #1**” and sent to Jackie Gapp, CFO, Fargo Public Schools, C/o McGough Construction, District Office, 700 7th St. S. Fargo, ND 58103. **Please indicate which Scope package number the proposal pertains to on the outside of the sealed envelope.**

***PLEASE NOTE* - Electronic proposals will NOT be accepted.**

Bidders submitting a bid must include all required documents listed below as separate attachments and name each attachment to properly identify them as listed below:

Documents required to be submitted with bid:

- Bid Form completed and Signed
- Bid Package Scope Form completed

A public bid opening will occur at 1:00 PM Thursday, January 9st, 2025 at the Fargo Public Schools District Office 700 7th ST. S. Fargo, ND 58103 or can be called into using the teams invite below.

***PLEASE NOTE* - Any proposals turned in at the 1:00PM Public Opening will not be accepted. Proposal must be submitted no later than 12:00PM January 9th.**

Microsoft Teams [Need help?](#)

[Join the meeting now](#)

Meeting ID: 252 262 235 611

Passcode: bC2E8t6X

Dial in by phone

[+1 412-912-1530,619914151#](tel:+14129121530619914151) United States, Pittsburgh

[Find a local number](#)

Phone conference ID: 619 914 151#

For organizers: [Meeting options](#) | [Reset dial-in PIN](#)

Pre Bid Meeting:

Optional prebid site visit and Q&A sessions are scheduled per the matrix below. All times are Central Time.

Site Location	Monday, December 23 rd	Tuesday, December 31 st
Longfellow Elementary 20 29 th Ave. NE Fargo, ND 58102	8:00 AM	8:00 AM
Lincoln Elementary 2120 9 th St. S. Fargo, ND 58103	9:00 AM	9:00 AM
Centennial Elementary 4201 25 th St. S. Fargo, ND 58104	10:00 AM	10:00 AM
Trollwood Performing Arts 801 50 th Ave. S Moorhead, MN 56560	11:00 AM	11:00 AM

Bidder Questions:

We will accept and respond to questions as quickly as possible up to the bid date. However, please try to have questions to McGough no later than **Tuesday, January 2nd, 2025**. We will issue these to the Architect for them to respond via addendum prior to the bid date. All questions received after the 2nd may not be answered before bid day.

Bidder questions can be submitted via email to brady.snell@mcgough.com

Contract:

McGough and Subcontractor agree that McGough's Standard Subcontract Agreement shall be the prescribed

subcontract form without modification. By submitting a proposal, Subcontractor acknowledges and agrees to all terms and conditions set forth in the Standard Subcontract Agreement included in the Bidding Documents. McGough must receive a fully executed Standard Subcontract Agreement and Certificate of Insurance prior to commencement of Work

Pre-Qualification Requirements:

McGough and Subcontractor agree that Subcontractor shall be required to provide prequalification information as defined by Contractor prior to Contract Award and at any time during the entire duration of the Contract. Prequalification information shall be provided in electronic format and shall be submitted to Contractor using the CMiC system prescribed by Contractor. Link: <https://www.mcgough.com/prequalifications>

If Subcontractor is notified of intent to award a subcontract, and Subcontractor has NOT completed their Prequalification, Subcontractor will have 10 days to complete prequalification or contract may be awarded to another subcontractor.

There are no fees and/or costs associated with Subcontractor's use of CMiC. However, if the pre-qualification requirement is not fulfilled, it will hinder Subcontractor from receiving any bid notifications and/or contracting work with McGough.

If you have any questions, regarding prequalification, please contact subprequal@mcgough.com

Other Comments:

If you have questions, please contact **Brady Snell @ 701.261.5270** or via email at brady.snell@mcgough.com

Project Information

McGough	Project:	Fargo Public Schools – Multiple Facility Project Bid Package #1	Physical Bids Due:	1/9/2025 @ 12pm Central
	Physical Bids Received by:	Fargo Public Schools District Office C/O McGough Construction 700 7 th St. S Fargo, ND 58103		

Sub	Contact:		Phone/Email:	
	Company:			

Tax Exempt **NO**
EEO Project Specific Requirements **NO**

The undersigned, as Subcontractor, hereby proposes, and if this Bid is accepted, agrees to furnish all Work as specified on this Bid Form for the construction of the Project.

General Requirements:

The Subcontractor agrees to perform all the Scope of Work as described in the Contract Documents and Specifications.

The Subcontractor attests to having carefully examined all Bid and Contract Documents prepared by Zerr Berg Architects and McGough and personally inspected the actual location of the Work and local sources of supply and is satisfied as to all the quantities and conditions. The Subcontractor understands that in signing this Bid Form all rights to plead any misunderstanding(s) regarding the same is waived.

The Subcontractor hereby proposes to furnish all labor, materials, taxes, tools, equipment, machinery, equipment rental, transportation, superintendence, perform all work, provide all services, and to completely construct the portion of work described above and for the Bid amount as stated below. The Bid amount is to cover all costs incurred in performing the Work in strict accordance with the plans and specifications for that Scope of Work category under the Contract Documents and Specifications, of which this Bid Form is a part. This work will be performed for the lump sum including any alternates and unit prices.

Pricing:

Bid Package:	
---------------------	--

Labor and Miscellaneous Taxable Material Total:		
	\$	
(SHOW AMOUNTS IN BOTH WORDS AND FIGURES. IN CASE OF A DISCREPANCY, THE AMOUNT SHOWN IN WORDS WILL GOVERN.)		

****McGough may request additional pricing breakdown following receipt of bid****

Required Bid Alternates	Amount	
Bennett Elementary – Salvage & Repurpose Subbase in lieu of Replacing.	\$	
Centennial Elementary School – Replace window wood blocking in lieu of repurpose	\$	
Eagles Elementary – Install rubberized play surfacing in lieu of repurposing existing	\$	
Lincoln Elementary – Bituminous Paving ion lieu of Concrete Paving	\$	
Longfellow Elementary – Install rubberized play surfacing in lieu of repurposing existing	\$	
North High School – Bituminous Paving in lieu of Concrete Paving (NE Lot)	\$	
North High School – Salvage & repurpose subbase in lieu of Replacing (NE Lot)	\$	
North Highschool – Bituminous Paving in lieu of Concrete Paving (Pedestrian path)	\$	
North Highschool – Remove & replace wood roof sheathing in lieu of repurpose. (Shed reroofing)	\$	
Trollwood – Bituminous Paving in lieu of Concrete Paving	\$	
Trollwood – Salvage & repurpose subbase in lieu of Replacing	\$	

Voluntary Alternates	Amount	
	\$	
	\$	
	\$	

Addenda Acknowledgement:

Subcontractor acknowledges receipt of following Addenda and has incorporated the requirements of the Addenda in the Bid. (Please list below.)

Addenda # _____, Addenda # _____, Addenda # _____, Addenda # _____, Addenda # _____

McGough Safety Standards:

Subcontractor acknowledges that they have read and can meet, and abide by, the McGough Safety Standards that are included with the Bid Documents, but any and all costs to do so are included in their bid proposals.

- YES, I read and can meet, and abide by, McGough Safety Standards and any and all costs associated with meeting these standards are included in this bid proposal.

McGough Prequalification Requirements:

McGough and Subcontractor agree that Subcontractor shall be required to provide prequalification information as defined by Contractor prior to Contract Award and at any time during the entire duration of the Contract.

Prequalification information shall be provided in electronic format and shall be submitted to Contractor using the CMiC system prescribed by Contractor. Link: [McGough Prequalification](#)

If Subcontractor is notified of intent to award a subcontract, and Subcontractor has **NOT** completed their Prequalification, Subcontractor will have 10 days to complete prequalification or contract may be awarded to another subcontractor.

- YES, I read and can meet, and abide by, McGough Prequalification Requirements

Subcontract Form/Insurance Requirements Agreement:

Subcontractor agrees to enter into the current McGough Standard Subcontract Agreements (Revised July 2015) without modification and acknowledges that they can meet the Insurance requirements listed in the McGough Standard Subcontract Agreements:

- YES, I agree. No exceptions taken.
- YES, I have a previously executed Master Agreement in place.

****Exceptions identified Post-Bid will NOT be taken into consideration, and may disqualify the bid, as determined solely by McGough.**

Bid Process:

McGough Construction will receive bids until:

Thursday, January 9th 2025 – 12:00 PM (Central)

Sealed proposals can be submitted with the Subject “**FPS- MSA – Bid Package #1**” and sent to Jackie Gapp, CFO, Fargo Public Schools, C/o McGough Construction, District Office, 700 7th St. S. Fargo, ND 58103. **Please indicate which Scope package number the proposal pertains to on the outside of the sealed envelope.**

***PLEASE NOTE* - Electronic proposals will NOT be accepted.**

Bidders submitting a bid must include all required documents listed below as separate attachments and name each attachment to properly Identify them as listed below:

Documents required to be submitted with bid:

- Bid Form completed and Signed
- Bid Package Scope Form completed

A public bid opening will occur at 1:00 PM Thursday, January 9th, 2025 at the Fargo Public Schools District Office 700 7th ST. S. Fargo, ND 58103 or can be called into using the teams invite below.

***PLEASE NOTE* - Any proposals turned in at the 1:00PM Public Opening will not be accepted. Proposal must be submitted no later than 12:00PM January 9th.**

Microsoft Teams [Need help?](#)

[Join the meeting now](#)

Meeting ID: 252 262 235 611

Passcode: bC2E8t6X

Dial in by phone

[+1 412-912-1530,619914151#](#) United States, Pittsburgh

[Find a local number](#)

Phone conference ID: 619 914 151#

For organizers: [Meeting options](#) | [Reset dial-in PIN](#)

Bidding Acceptance Period:

Subcontractors shall agree not to withdraw bids for a period of *sixty (60)* days after date of opening of bids. Bidding award is anticipated to take place by **February 15th, 2025**.


In submitting this bid, it is understood that McGough and Owner reserves the right to reject any or all bids, to waive any informality or irregularity in any bid received.

THE UNDERSIGNED operates as a:

Sole Owner
 Partnership
 Corporation incorporated in the State of _____

Other (Specify) _____

LEGAL NAME OF PERSON, FIRM OR CORPORATION:			
Name			
Address			
Phone		Email	
By		Title	
By		Title	

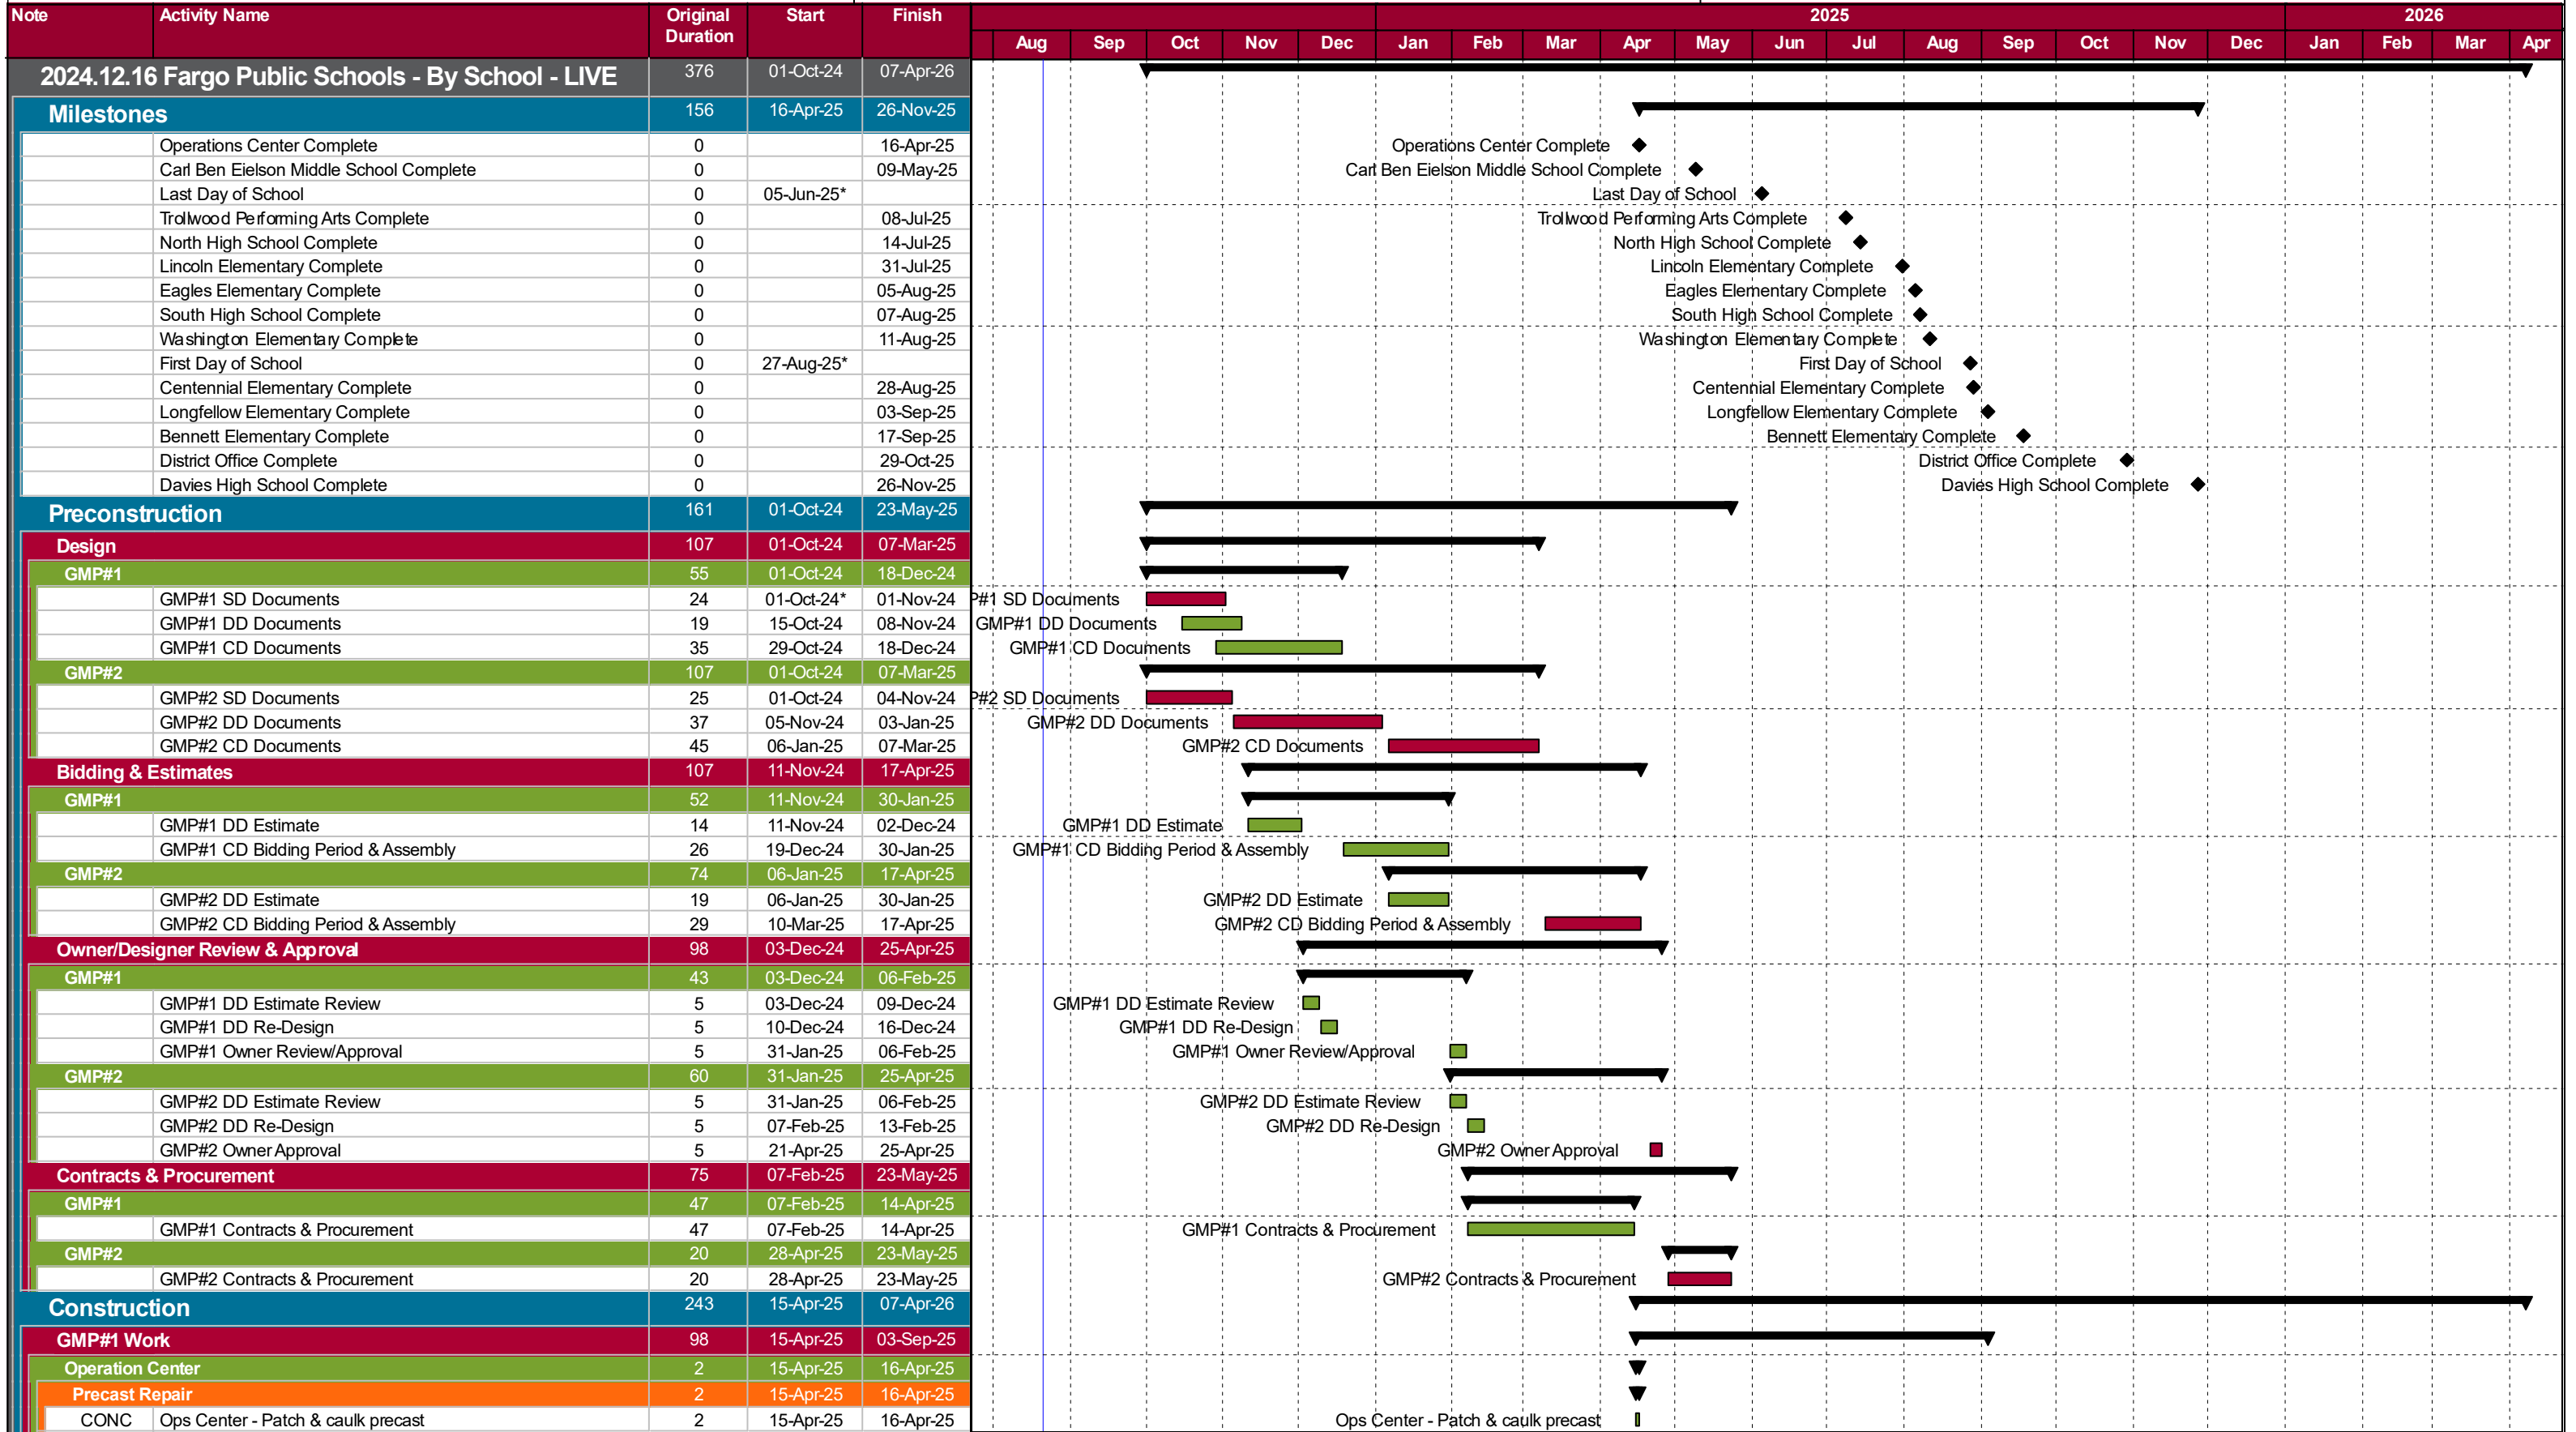

- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone
- Summary

2024.12.16 Fargo Public Schools - By School - LIVE
***** Fargo Public Schools Multiple Services DD Schedule *****
16-Dec-24



Note	Activity Name	Original Duration	Start	Finish	2025												2026						
					Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb
	Trollwood Performing Arts	58	15-Apr-25	08-Jul-25																			
	Portable Class Rooms	18	15-Apr-25	09-May-25																			
	Sidewalks	2	15-Apr-25	16-Apr-25																			
	CONC Added Trollwood - Grind down walkways	2	15-Apr-25	16-Apr-25																			
	General	18	15-Apr-25	09-May-25																			
	CARP Trollwood - Replace wood trim, deck, handrail	8	15-Apr-25	25-Apr-25																			
	PAINT Trollwood - Stain, paint portable classrooms	3	28-Apr-25	30-Apr-25																			
	MECH Trollwood - Replace domestic water heater	2	01-May-25	02-May-25																			
	ELECT Trollwood - Replace fluorescent light fixtures	2	05-May-25	06-May-25																			
	FLOOR Trollwood - Replace carpet at portable classrooms	3	07-May-25	09-May-25																			
	Wood Arch Refurbishment	40	12-May-25	08-Jul-25																			
	PAINT Trollwood - Refinish wood laminate arches	40	12-May-25	08-Jul-25																			
	CARP Trollwood - Remove front row(s) seating for access	5	12-May-25	16-May-25																			
	Parking Lots	27	15-Apr-25	22-May-25																			
	South Parking Lot Replacement	27	15-Apr-25	22-May-25																			
	EXCAV Trollwood - Demo, subgrade & compact	5	15-Apr-25	22-Apr-25																			
	CONC Trollwood - Concrete paving	20	23-Apr-25	20-May-25																			
	STRIP Trollwood - Striping	1	21-May-25	21-May-25																			
	LAND Trollwood - Seed	1	22-May-25	22-May-25																			
	Grass Parking Lot Reinforcement	10	23-Apr-25	06-May-25																			
	EXCAV Trollwood - Replace south paved lot & grass parking lot	10	23-Apr-25	06-May-25																			
	North High	62	15-Apr-25	14-Jul-25																			
	Track Building Roof Replacement	20	15-Apr-25	13-May-25																			
	ROOF North HS - Replace shingles, evaluate metal roof consideration	20	15-Apr-25	13-May-25																			
	Sidewalk/Concrete Replacement	17	21-May-25	13-Jun-25																			
	CONC North HS - Remove/replace west sidewalk	8	21-May-25	02-Jun-25																			
	CONC North HS - Remove/replace north sidewalk	8	03-Jun-25	12-Jun-25																			
	LAND North HS - Seed	1	13-Jun-25	13-Jun-25																			
	Parking Lot	27	05-Jun-25	14-Jul-25																			
	NE Parking Lot Patching	6	05-Jun-25	12-Jun-25																			
	ASPH North NS - Patch parking lot	6	05-Jun-25	12-Jun-25																			
	NW Parking Lot Replacement	27	05-Jun-25	14-Jul-25																			
	EXCAV North HS - Demo, subgrade & compact	5	05-Jun-25	11-Jun-25																			
	CONC North HS - Concrete paving	20	12-Jun-25	10-Jul-25																			
	STRIP North HS - Striping	1	11-Jul-25	11-Jul-25																			
	LAND North HS - Seed	1	14-Jul-25	14-Jul-25																			
	Fire Device Replacement	15	05-Jun-25	25-Jun-25																			
	ELECT North HS - Replace fire devices	15	05-Jun-25	25-Jun-25																			
	Control Panel Replacement	5	26-Jun-25	02-Jul-25																			
	ELECT North HS - Replace (1) control panel	5	26-Jun-25	02-Jul-25																			
	Parking Lot Lighting Replacement	10	15-Apr-25	29-Apr-25																			
	ELECT North HS - Replace existing parking lot light fixtures to LED	10	15-Apr-25	29-Apr-25																			
	South High	70	30-Apr-25	07-Aug-25																			
	Parking Lot Lighting Replacement	10	30-Apr-25	13-May-25																			
	ELECT South High - Replace existing parking lot lighting fixture heads	10	30-Apr-25	13-May-25																			
	Gymastics Building Downspout Replacement/Repair	10	14-May-25	28-May-25																			
	ROOF South HS - Replacement of rain gutter & downspout system	10	14-May-25	28-May-25																			
	Track Surface Replacement	35	12-Jun-25	31-Jul-25																			
	EXCAV South HS - Demo, subgrade & compact	10	12-Jun-25	25-Jun-25																			
	ASPH South HS - Asphalt base	5	26-Jun-25	02-Jul-25																			
	TRACK South HS - Track surface struct spray & striping	20	03-Jul-25	31-Jul-25																			
	Fire Device Replacement	25	03-Jul-25	07-Aug-25																			
	ELECT South HS - Replace fire devices	15	03-Jul-25	24-Jul-25																			
	ELECT South HS - Replace (1) fire panel	10	25-Jul-25	07-Aug-25																			
	Cennntennial Elementary	95	15-Apr-25	28-Aug-25																			

- █ Actual Work
- █ Remaining Work
- █ Critical Remaining Work
- ◆ Milestone
- ┆ Summary

2024.12.16 Fargo Public Schools - By School - LIVE

*** Fargo Public Schools Multiple Services DD Schedule ***

16-Dec-24



Note	Activity Name	Original Duration	Start	Finish	2025												2026											
					Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr			
Window Replacement																												
PRO	Centennial Elem - 12 weeks procurement	95	15-Apr-25	28-Aug-25																								
CARP	Centennial Elem - Window replacement	60	15-Apr-25	10-Jul-25																								
CARP	Centennial Elem - Window finishes (sills, blinds, paint)	30	11-Jul-25	21-Aug-25																								
CARP	Centennial Elem - Window finishes (sills, blinds, paint)	15	08-Aug-25	28-Aug-25																								
Boiler Replacement																												
MECH	Centennial Elem - Replace (1) boiler	25	05-Jun-25	10-Jul-25																								
MECH	Centennial Elem - Replace hot water boiler unit at mezzanine	10	05-Jun-25	18-Jun-25																								
MECH	Centennial Elem - Replace hot water boiler unit at mezzanine	15	19-Jun-25	10-Jul-25																								
Remove Duel Fuel Tank																												
MECH	Centennial Elem - Demo existing duel fuel	5	11-Jul-25	17-Jul-25																								
Air Handling Unit Replacement																												
PRO	Centennial Elem - AHU Procurement	78	15-Apr-25	05-Aug-25																								
MECH	Centennial Elem - Demo old AHU	50	15-Apr-25	25-Jun-25																								
MECH	Centennial Elem - Demo old AHU	5	26-Jun-25	02-Jul-25																								
CONC	Centennial Elem - Housekeeping pad	3	03-Jul-25	08-Jul-25																								
MECH	Centennial Elem - Install new AHU	10	09-Jul-25	22-Jul-25																								
CARP	Centennial Elem - Finishes	10	23-Jul-25	05-Aug-25																								
Bennett Elementary																												
ELECT	Bennett Elem - Replace existing parking lot light fixtures to LED	10	14-May-25	28-May-25																								
Driveway Replacement																												
EXCAV	Bennett Elem - Demo, subgrade & compact	17	15-Jul-25	06-Aug-25																								
CONC	Bennett Elem - Concrete paving	5	15-Jul-25	21-Jul-25																								
CONC	Bennett Elem - Concrete paving	10	22-Jul-25	04-Aug-25																								
STRIP	Bennett Elem - Striping	1	05-Aug-25	05-Aug-25																								
LAND	Bennett Elem - Seed	1	06-Aug-25	06-Aug-25																								
Hot/Chilled Water Pumps Replacement																												
MECH	Bennett Elem - Replace (4) hot/chilled water pumps	10	15-Apr-25	29-Apr-25																								
Unit Heaters																												
MECH	Bennett Elem - Replace (3) additional unit heaters	5	30-Apr-25	06-May-25																								
Lincoln Elementary																												
Sidewalk Repair																												
CONC	Lincoln Elem - Grind down walkways	2	17-Apr-25	21-Apr-25																								
Parking Lot Replacement																												
EXCAV	Lincoln Elem - Demo, subgrade & compact	20	22-Jul-25	18-Aug-25																								
CONC	Lincoln Elem - Concrete paving	5	22-Jul-25	28-Jul-25																								
CONC	Lincoln Elem - Concrete paving	8	05-Aug-25	14-Aug-25																								
STRIP	Lincoln Elem - Striping	1	15-Aug-25	15-Aug-25																								
LAND	Lincoln Elem - Seed	1	18-Aug-25	18-Aug-25																								
Boiler Replacement																												
MECH	Lincoln Elem - Replace (1) boiler	10	18-Jul-25	31-Jul-25																								
Davies High																												
Track Surface Replacement																												
TRACK	Davies HS - Track surface struct spray & striping	10	05-Jun-25	18-Jun-25																								
Eagles Elementary																												
Playground Replacement & Related Concrete Work																												
EXCAV	Eagles Elem - Demo old portion of existing playground	28	26-Jun-25	05-Aug-25																								
EXCAV	Eagles Elem - Demo old portion of existing playground	3	26-Jun-25	30-Jun-25																								
EXCAV	Eagles Elem - New playground sub-base	3	01-Jul-25	03-Jul-25																								
PLAY	Eagles Elem - New playground equipment (includes piers)	5	07-Jul-25	11-Jul-25																								
CONC	Eagles Elem - New sidewalk FRP	5	07-Jul-25	11-Jul-25																								
CONC	Eagles Elem - New concrete SOG for rubberized surface	10	14-Jul-25	25-Jul-25																								
PLAY	Eagles Elem - New playground rubberized surface	7	28-Jul-25	05-Aug-25																								
Longfellow Elementary																												
Playground Surface Replacement																												
EXCAV	Longfellow Elem - Demo playground surfacing	29	07-Jul-25	14-Aug-25																								
EXCAV	Longfellow Elem - Demo playground surfacing	3	07-Jul-25	09-Jul-25																								
EXCAV	Longfellow Elem - New playground sub-base	3	10-Jul-25	14-Jul-25																								
CONC	Longfellow Elem - New concrete SOG for rubberized surface	5	28-Jul-25	01-Aug-25																								
PLAY	Longfellow Elem - New playground rubberized surfacing	7	06-Aug-25	14-Aug-25																								
Boiler Replacement																												
MECH	Longfellow Elem - Replace (1) boiler	20	01-Aug-25	28-Aug-25																								

█ Actual Work
█ Remaining Work
█ Critical Remaining Work
◆ Milestone
▬ Summary

2024.12.16 Fargo Public Schools - By School - LIVE
***** Fargo Public Schools Multiple Services DD Schedule *****
16-Dec-24




Note	Activity Name	Original Duration	Start	Finish	2025												2026						
					Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb
	MECH Longfellow Elem - Replace (3) boilers	20	01-Aug-25	28-Aug-25																			
	Water Heater Replacement	3	29-Aug-25	03-Sep-25																			
	MECH Longfellow Elem - Replace domestic water heater	3	29-Aug-25	03-Sep-25																			
	Carl Ben Etelson	25	07-May-25	11-Jun-25																			
	Parking Lot Lighting Replacement	10	29-May-25	11-Jun-25																			
	ELECT Carl Ben Elem - Replace existing parking lot light fixtures & wal	10	29-May-25	11-Jun-25																			
	Unit Heater Replacement	3	07-May-25	09-May-25																			
	MECH Carl Ben Elem - Replace (2) unit heaters	3	07-May-25	09-May-25																			
	Washington Elementary	6	05-Aug-25	12-Aug-25																			
	North Sidewalks Repair/Replacement	6	05-Aug-25	12-Aug-25																			
	CONC Washington Elem - Patch north section of sidewalks	5	05-Aug-25	11-Aug-25																			
	LAND Washington Elem - Seed	1	12-Aug-25	12-Aug-25																			
	GMP#2 Work	215	27-May-25	07-Apr-26																			
	District Offices	215	27-May-25	07-Apr-26																			
	Mechanical	100	27-May-25	15-Oct-25																			
	Boiler & Pump Replacement	25	27-May-25	30-Jun-25																			
	MECH District Office - Replace (2) boilers, (4) hot water pumps & boile	25	27-May-25	30-Jun-25																			
	Water Heater Replacement	5	01-Jul-25	08-Jul-25																			
	MECH District Office - Replace water heater	5	01-Jul-25	08-Jul-25																			
	VFD Replacement	25	09-Jul-25	12-Aug-25																			
	MECH District Office - Replace (2) VFDs (All VFDs)	25	09-Jul-25	12-Aug-25																			
	Exhaust Fan Replacement	15	13-Aug-25	03-Sep-25																			
	MECH District Office - Replace (5) exhaust fans	15	13-Aug-25	03-Sep-25																			
	Condenser Unit Replacement	15	04-Sep-25	24-Sep-25																			
	MECH District Office - Remove/Replace (4) Condenser Units	15	04-Sep-25	24-Sep-25																			
	AHU Coile Replacement	15	25-Sep-25	15-Oct-25																			
	MECH District Office - Replace (3) AHU Coils	15	25-Sep-25	15-Oct-25																			
	Electrical	215	27-May-25	07-Apr-26																			
	Feeder Conductor Replacement	15	27-May-25	16-Jun-25																			
	ELECT District Office - Replace Feeder Conductors	15	27-May-25	16-Jun-25																			
	Wall Pack Replacement	5	17-Jun-25	23-Jun-25																			
	ELECT District Office - Replace exterior wall packs	5	17-Jun-25	23-Jun-25																			
	Branch Panel Replacement	15	24-Jun-25	15-Jul-25																			
	ELECT District Office - Replace Electrical Branch Panels	15	24-Jun-25	15-Jul-25																			
	Elect Distribution Replacement	215	27-May-25	07-Apr-26																			
	PRO District Office - Switchgear Procurement	200	27-May-25	16-Mar-26																			
	ELECT District Office - Replace site electrical distribution	15	17-Mar-26	07-Apr-26																			
	Building Controls	50	20-Aug-25	29-Oct-25																			
	Building Controls Replacement	50	20-Aug-25	29-Oct-25																			
	CONT District Office - Replace Honeywell BAS & upgrade HVAC cont	50	20-Aug-25	29-Oct-25																			
	South High	30	27-May-25	08-Jul-25																			
	CMU Foundation Repair	30	27-May-25	08-Jul-25																			
	MASON South HS - Shore & repair CMU	30	27-May-25	08-Jul-25																			
	Bennett Elementary	80	27-May-25	17-Sep-25																			
	Electronic Sign	80	27-May-25	17-Sep-25																			
	PRO Bennett Elem - Sign Procurement	70	27-May-25	03-Sep-25																			
	SIGN Bennett Elem - Replace existing sign with electronic sign	10	04-Sep-25	17-Sep-25																			
	Exterior Walls	60	27-May-25	19-Aug-25																			
	PRO Bennett Elem - Storefront Procurement	40	27-May-25	22-Jul-25																			
	WDW Bennett Elem - Replace (1) storefront	5	23-Jul-25	29-Jul-25																			
	CAULK Bennett Elem - Replace caulking/expansion joints	15	30-Jul-25	19-Aug-25																			
	EFIS Bennett Elem - Demo & replace EFIS and associated flashings	8	30-Jul-25	08-Aug-25																			
	MASON Bennett Elem - Repair Brick	5	30-Jul-25	05-Aug-25																			
	PAINT Bennett Elem - Paint Columns	5	13-Aug-25	19-Aug-25																			

- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone
- Summary

2024.12.16 Fargo Public Schools - By School - LIVE
***** Fargo Public Schools Multiple Services DD Schedule *****
 16-Dec-24



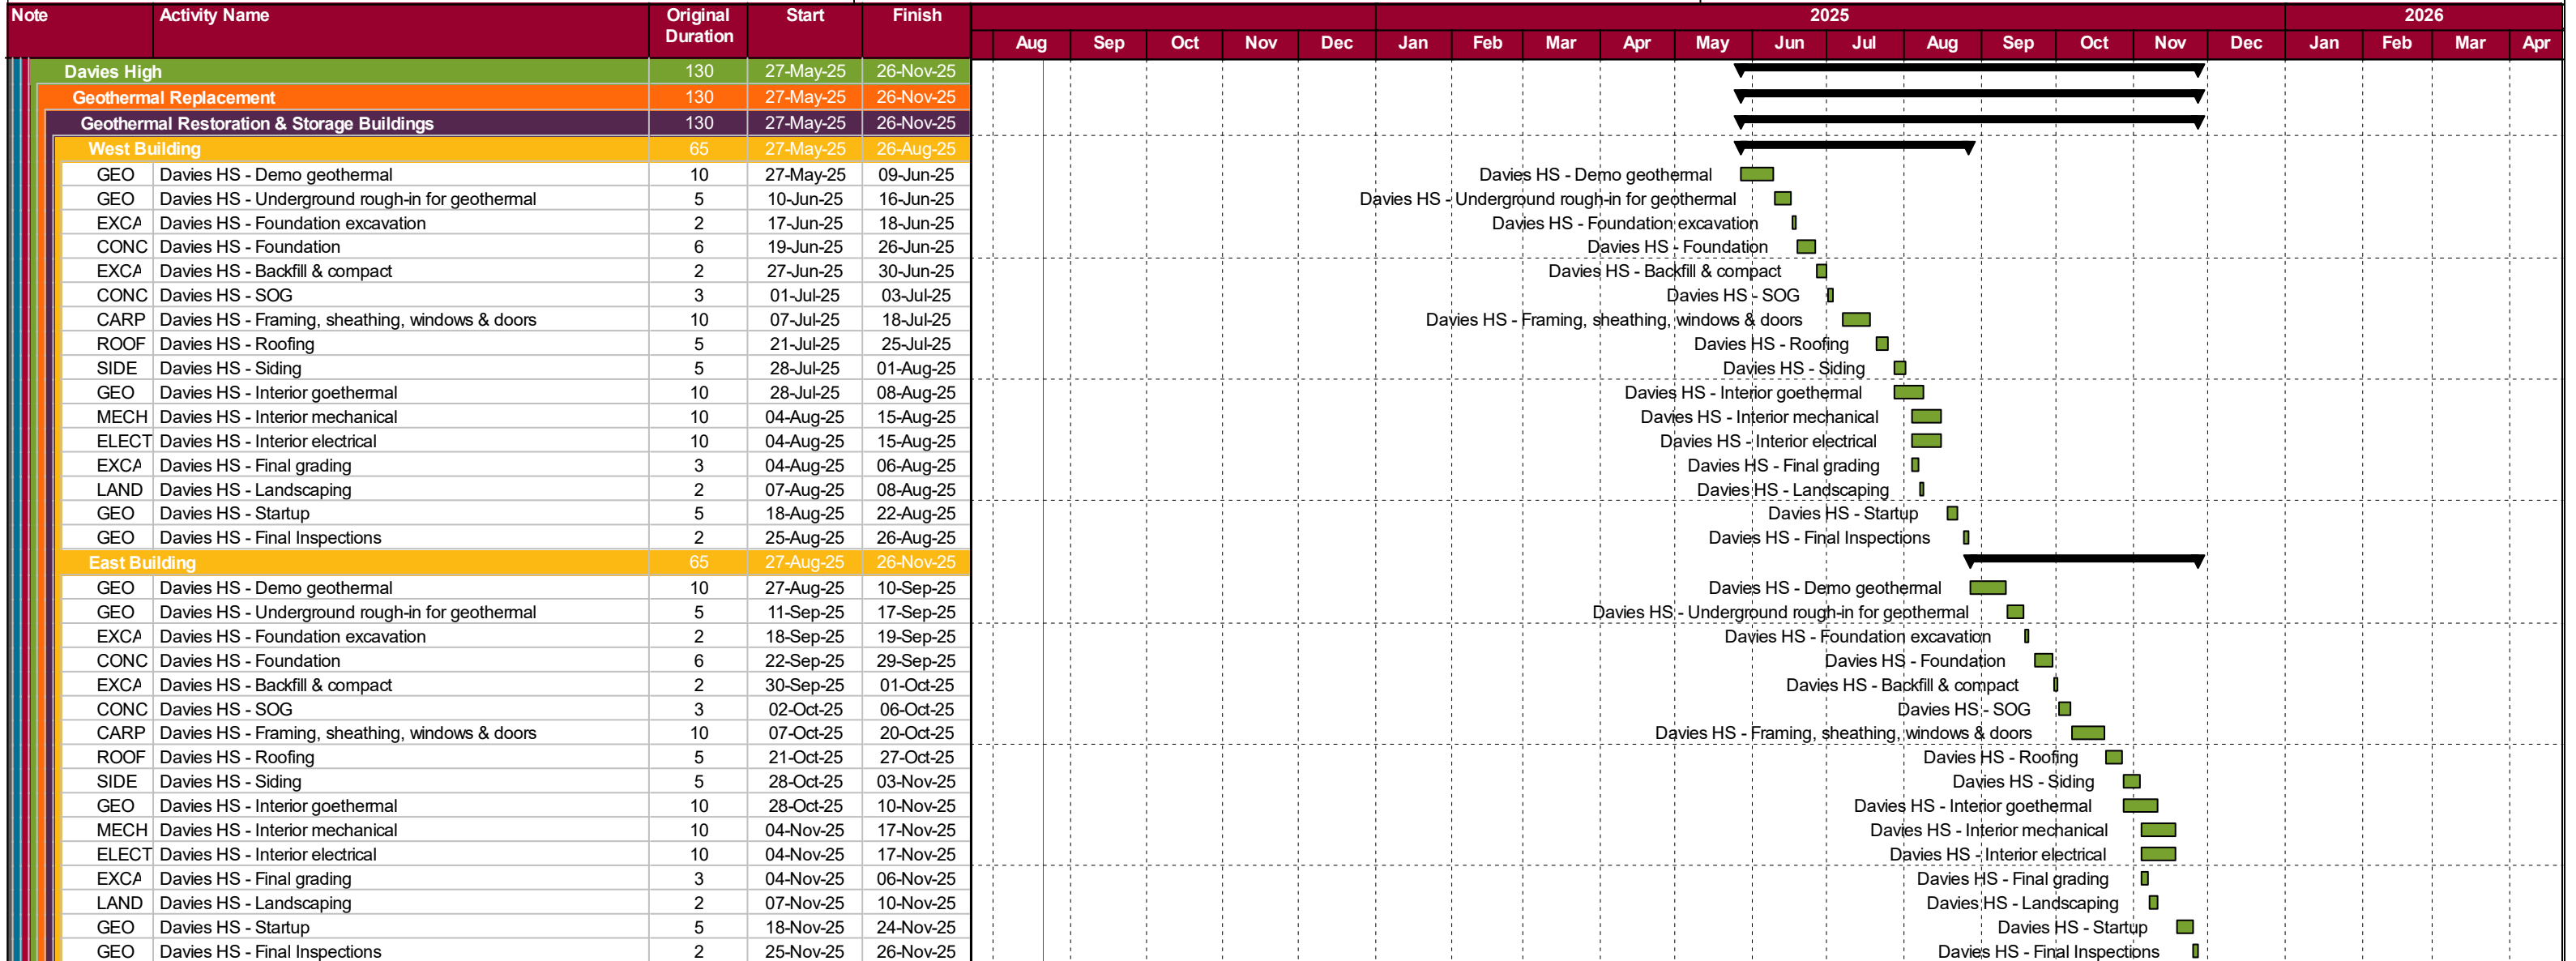

- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone
- Summary

2024.12.16 Fargo Public Schools - By School - LIVE
***** Fargo Public Schools Multiple Services DD Schedule *****
16-Dec-24

